



# TEXAS 2027-2030 STIP DEVELOPMENT SCHEDULE

Phase	Development Activities	Month Due	Duration	Agency Responsible/Involved					
				TxDOT		MPO	RTPO	USDOT	
				Division	District			FHWA	FTA
Preliminary	<b>MPO Project Consultation Period</b> TxDOT Districts and Metropolitan Planning Organizations (MPOs) consulting with Urban, Tribal, and Public Transportation partners for 2027-2030 project list. <i>Source: MTP.</i>								
	<b>MPO Draft 2027 - 2030 TIP Development</b> TxDOT Districts and MPOs advance project list to Draft 2027-2030 TIP.	Feb. 2026	3 months*						
	<b>Rural Draft 2027 - 2030 TIP Development</b> TxDOT Districts consult with Rural, Tribal, and Public Transportation partners for Draft 2027-2030 TIP.	Feb. 2026	3 months*						
	<b>State / Federal Agency Project Consultation Period</b> TPP to coordinate with TPWD and Federal agencies for 2027-2030 projects.	Feb. 2026	2 weeks						
	<b>Coordinated Review (Compliance Review): Project Data / Fiscal Analysis</b> Districts and MPOs review project data, groupability, air quality fields (as applicable), and fiscal constraint. Ensure fields are correct and grouping of projects is used to maximum extent allowable. Complete TIP Checklist.	Feb. 2026	1 month						
Draft 1 TIP	<b>Draft 1: 2027 - 2030 TIP Submittal</b> Draft 1 2027-2030 TIP includes correct project data, demonstration of fiscal constraint, and documentation indicating District-MPO coordination. Ensure TIP project information is an exact match of MTP project information and conformity documentation (as applicable). <i>TIP Checklist completed by Districts and MPOs (as applicable).</i>	Feb. 2026	1 month						
	<b>Draft 1: 2027 - 2030 TIP Review</b> Review project data, grouping, air quality fields (as applicable), and fiscal constraint. TPP conduct preliminary statewide Financial Analysis. USDOT invited for informal review.	Apr. 2026	5 weeks						
	<b>Draft 1: 2027 - 2030 TIP Returned to Districts and MPOs</b> TPP comments addressing project data, groupability, air quality fields (as applicable), and fiscal constraint returned to Districts and MPOs.	Apr. 2026	1 day						
	<b>Draft 1: 2027 - 2030 TIP Revisions</b> Districts and MPOs to address TPP comments on Draft 1 2027-2030 TIP. Local coordination as applicable. Initiate Public Involvement.	Apr. 2026	2 weeks						
Draft 2 TIP	<b>Draft 2: 2027 - 2030 TIP Submittal</b> Draft 2 TIP with TPP comments addressed.	Apr. 2026	2 weeks						
	<b>Draft 2: 2027 - 2030 TIP Review</b> Review project data, air quality fields (as applicable), and fiscal constraint. TPP conduct preliminary statewide Financial Analysis. USDOT invited for informal review.	May 2026	1 month						
	<b>Draft 2: 2027 - 2030 TIP Returned to Districts and MPOs</b> TPP and USDOT comments addressing project data, groupability, air quality fields (as applicable), and fiscal constraint returned to Districts and MPOs.	May 2026	1 day						
	<b>Draft 2: 2027 - 2030 TIP Revisions</b> Districts and MPOs resolve comments on Draft 2 TIP. Local coordination as applicable. Projects with TPP-identified issues may not be advanced into the 2027-2030 STIP.	May 2026	2 weeks						
Final STIP	<b>Final 2027 - 2030 TIP Submittal</b> Districts and MPOs submit Final TIPs in eSTIP. <i>Certified TIP Checklist completed by Districts and MPOs (as applicable).</i>	May 2026	3 weeks						
	<b>Final 2027 - 2030 STIP Development</b> TPP finalizes STIP, Statewide Financial Summary, and demonstration of Fiscal Constraint. Notify GCD-Tx Registry, prepare website for publishing, and prepare for public hearing.	June 2026	2 weeks						
	<b>Final 2027 - 2030 STIP Public Involvement</b> 30 day public comment period with virtual public hearing.	July 2026	1 month						
	<b>Final 2027 - 2030 STIP Submitted</b> Close out public involvement. Route STIP from TxDOT Executive Director to USDOT for approval.	July 2026	1 day						
	<b>Letting</b> TPP notify FIN Letting Management of approved STIP. Letting Schedule developed based on STIP approved projects.	July 2026	1 day						

\* Varies by MPO and District.

Schedule is subject to change.

# TEXAS 2027-2030 STIP DEVELOPMENT SCHEDULE

NOV 2025 - FEB 2026

FEB 2026 - APR 2026

APR 2026 - MAY 2026

JUN 2026 - JUL 2026



## PRELIMINARY PHASE

- **MPO Project Consultation Period**
  - TxDOT Districts and MPOs consulting with Urban, Tribal, and Public Transportation partners for 2027-2030 project list. *Source: MTP.*
- **MPO Draft 2027-2030 TIP Development**
  - 11/04/25 - 2/10/26 (3 months\*)
  - TxDOT Districts and MPOs advance project list to Draft 2027-2030 TIP.
- **Rural Draft 2027-2030 TIP Development**
  - 11/04/25 - 2/10/26 (3 months\*)
  - TxDOT Districts consult with Rural, Tribal, and Public Transportation partners for Draft 2027-2030 TIP.
- **State / Federal Agency Project Consultation**
  - 01/27/26 - 2/10/26 (2 weeks)
  - TPP to coordinate with TPWD and Federal agencies for 2027-2030 projects.
- **Coordinated Review (Compliance Review): Project Data / Fiscal Analysis**
  - 2/02/26 - 2/27/26 (1 month)
  - Districts and MPOs review project data, groupability, air quality fields (as applicable), and fiscal constraint.
  - Ensure fields are correct and grouping of projects is used to maximum extent allowable.
  - Complete TIP Checklist.

\* Varies by MPO and District.

## DRAFT 1 TIP

- **Draft 1: 2027-2030 TIP Submittal**
  - 02/02/26 - 02/27/26 (1 month)
  - Includes correct project data, demonstration of fiscal constraint, and documentation indicating District-MPO coordination.
  - Ensure TIP project information is an exact match of MTP project information and conformity documentation (as applicable).
  - *TIP Checklist completed by Districts and MPOs (as applicable).*
- **Draft 1: 2027-2030 TIP Review**
  - 03/02/26 - 04/02/26 (5 weeks)
  - Review project data, grouping, air quality fields (as applicable), and fiscal constraint.
  - TPP conduct preliminary statewide Financial Analysis.
  - USDOT invited for informal review.
- **Draft 1: 2027-2030 TIP Returned to Districts and MPOs**
  - 04/03/26 - 04/03/26 (1 day)
  - TPP comments addressing project data, groupability, air quality fields (as applicable), and fiscal constraint returned to Districts and MPOs.
- **Draft 1: 2027-2030 TIP Revisions**
  - 04/06/26 - 04/17/26 (2 weeks)
  - Districts and MPOs to address TPP comments on Draft 1 2027-2030 TIP.
  - Local coordination as applicable.
  - Initiate Public Involvement.

## DRAFT 2 TIP

- **Draft 2: 2027-2030 TIP Submittal**
  - 04/06/26 - 04/17/26 (2 weeks)
  - Submit Draft 2 TIP with TPP comments addressed.
- **Draft 2: 2027-2030 TIP Review**
  - 04/20/26 - 05/15/26 (1 month)
  - Review project data, air quality fields (as applicable), and fiscal constraint.
  - TPP conduct preliminary statewide Financial Analysis.
  - USDOT invited for informal review.
- **Draft 2: 2027-2030 TIP Returned to Districts and MPOs**
  - 05/15/26 - 05/15/26 (1 day)
  - TPP and USDOT comments addressing project data, groupability, air quality fields (as applicable), and fiscal constraint returned to Districts and MPOs.
- **Draft 2: 2027-2030 TIP Revisions**
  - 05/18/26 - 05/29/26 (2 weeks)
  - Districts and MPOs resolve comments on Draft 2 TIP.
  - Local coordination as applicable.
  - Projects with TPP-identified issues may not be advanced into the 2027-2030 STIP.

## FINAL STIP

- **Final: 2027-2030 TIP Submittal**
  - 05/11/26 - 05/29/26 (3 weeks)
  - Districts and MPOs submit Final TIPs in eSTIP.
  - *Certified TIP Checklist by Districts and MPOs (as applicable).*
- **Final: 2027-2030 STIP Development**
  - 06/01/26 - 06/12/26 (2 weeks)
  - TPP compiles TIPs into STIP, finalize Statewide Financial Summary and Fiscal Constraint demonstration.
  - Notify GCD-Tx Registry, prepare website for publishing, and prepare for public hearing.
- **Final: 2027-2030 STIP Public Involvement**
  - 06/13/26 - 07/12/26 (1 month)
  - 30 day public comment period with a virtual public hearing.
- **Final: 2027-2030 STIP Submitted**
  - 07/13/26 - 07/13/26 (1 day)
  - Close out public involvement.
  - Route STIP from TxDOT Executive Director to USDOT for approval.
- **Letting**
  - 07/14/26 - 07/14/26 (1 day)
  - TPP notify FIN Letting Management of approved STIP.
  - Letting Schedule developed based on STIP approved projects.


### TASK OWNER

- TxDOT District
- Metropolitan Planning Organization (MPO)
- USDOT FHWA
- TxDOT Division
- Regional Transportation Planning Organization (RTPO)
- USDOT FTA

*Schedule is subject to change.*



# TEXAS 2027-2030 STIP DEVELOPMENT SCHEDULE

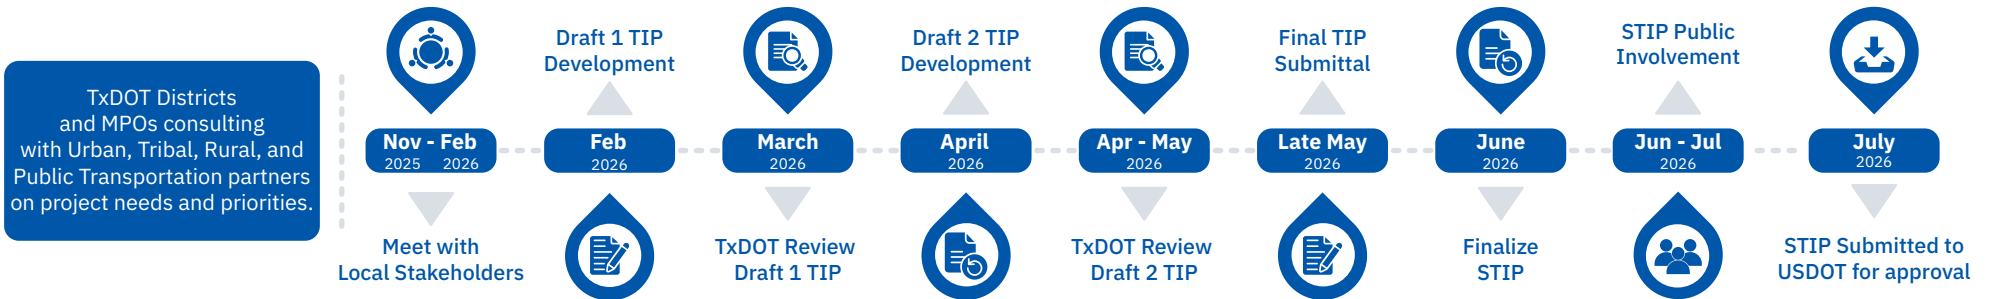


Schedule is subject to change.



# TEXAS 2027-2030 STIP DEVELOPMENT SCHEDULE WITH REVISIONS

During 2026: February Revision 25-28, Limited May Revision 25-28, Initial 27-30, and Adjusted November Revision 27-30

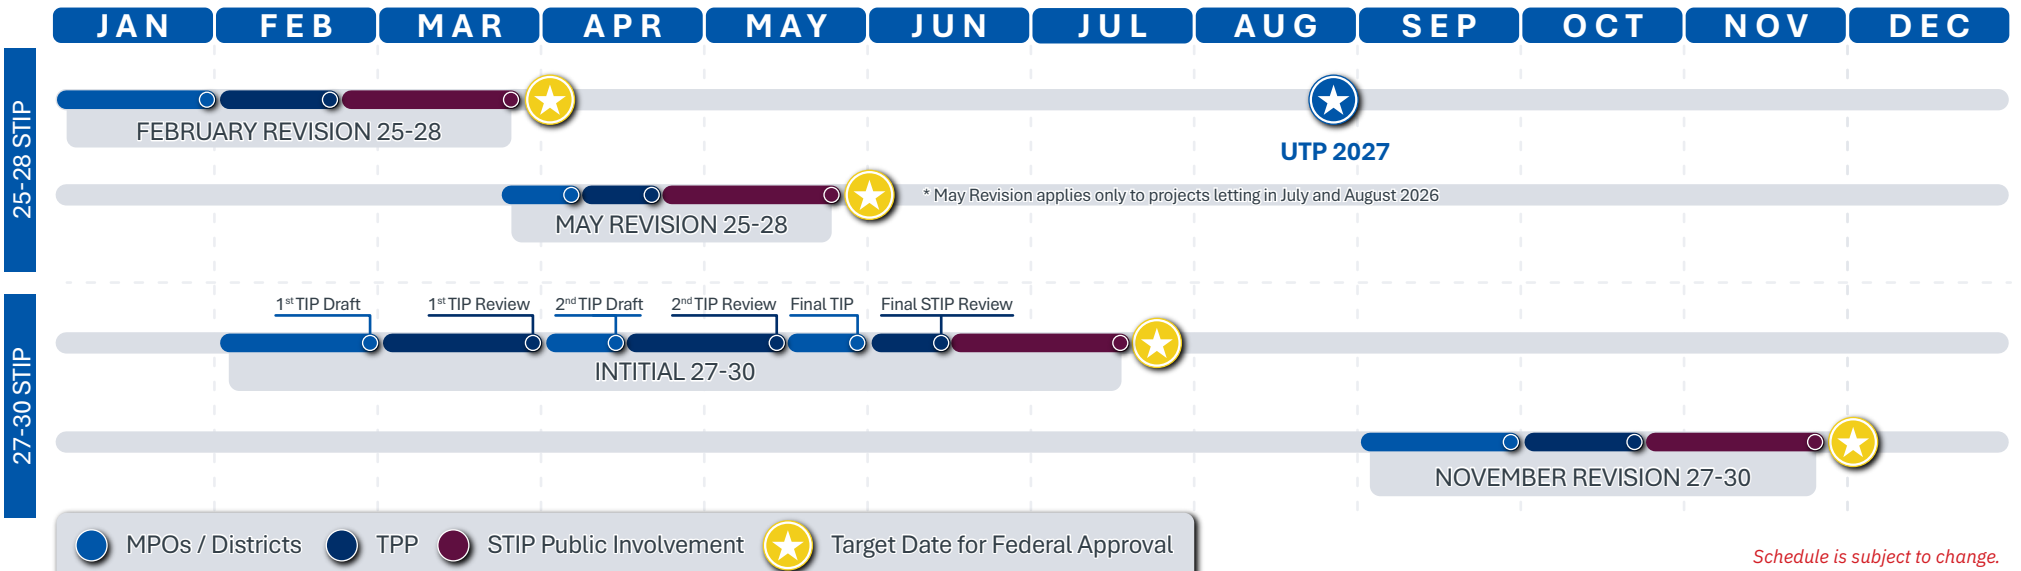

Schedule is subject to change.
